

# PROJECT UPDATE

Issue No. 02  
April 2018

2017 Capital Campaign & Building Project



Establishing building corners  
04.24.2018



Trench for Building Utilities  
05.05.2018



Removal & Stockpiling of Topsoil at Future Detention Pond \_ 05.05.2018



Trenching Equipment Delivered to Site  
04.21.2018



Building Pad Finalized  
04.15.2018



Road between parking zones razed  
04.11.2018

## Progress to Date

### St. Dymphna Center:

- Job trailer delivered to the site
- Road path connecting parking zones razed
- Building pad finalized and ready to receive all foundation formwork and building utility lines.
- Trenching equipment delivered to site
- Building corners established.
- Engineering and layout to begin
- Trenching for building & site utilities to begin
- Site work subcontractor continues work around building pad
- Removal and stockpiling of topsoil at future detention pond completed


## Looking Ahead:

### St. Dymphna Center:

- Continue building and site utilities trenching.
- Begin of building foundation formwork.
- Continue underfloor plumbing & electrical rough-in.
- Begin boring under Ranch Road 12 to connect to the City waste water line.
- First concrete foundation pour scheduled.
- Pre-engineered metal building delivery scheduled.

## Graph Legend

- GMP Money Authorized to Date
- Completion of Projects
- Schedule for Projects

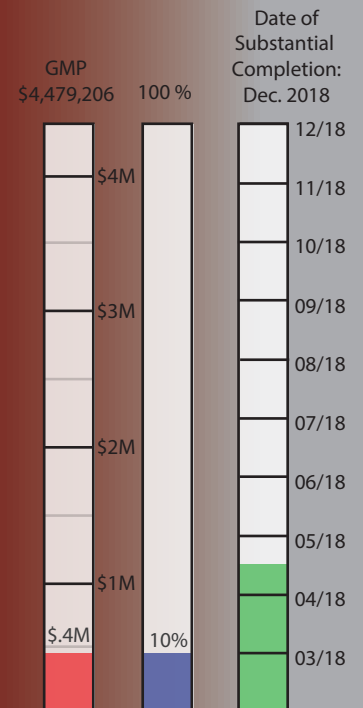

\*Summary of Total Project Cost \$5.4M



**ST. DYMPHNA CENTER**  
ST. MARTIN DE PORRES CATHOLIC CHURCH

