

PROJECT UPDATE

Issue No. 04
June 2018

2017 Capital Campaign & Building Project



Continuation of Metal Building Steel Erection
06.28.2018



Continuation of Metal Building Steel Erection
07.05.2018



Continuation of Metal Building Steel Erection
06.27.2018



Begin of Metal Building Steel Erection
06.26.2018



Stage/Altar Finalized
06.25.2018

Progress to Date

St. Dymphna Center:

- Concrete pour of canopy sidewalks and stage/altar completed.
- Trenching under Ranch Road 12 for site utilities completed.
- Began pre-engineered metal building steel erection.
- Began roof purlins, wall girts, and miscellaneous steel supports.


Graph Legend

- █ GMP Money Authorized to Date
- █ Completion of Projects
- █ Schedule for Projects

Looking Ahead:

St. Dymphna Center:

- Complete installation of site utilities
- Complete steel installation
- Continue building plumbing & electrical rough-in
- Continue site work and flatwork preparation
- Continue of metal building structure erection
- Continue detention pond storm sewer installation
- Begin metal stud framing installation
- Begin roof & wall insulation installation
- Begin roof deck over office area.
- Begin installation of communication systems
- Razing of Parish Office Building

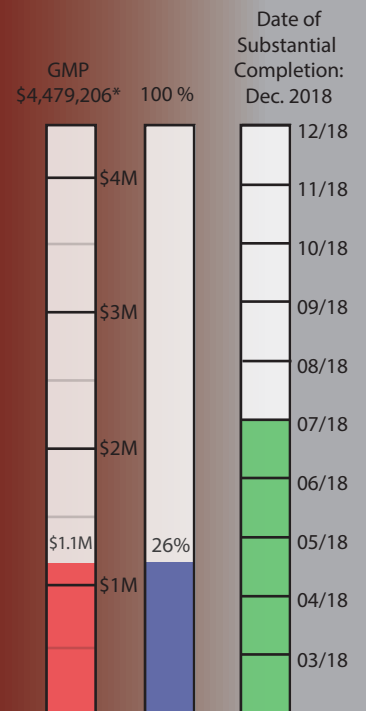

*Summary of Total Project Cost \$5.4M



ST. DYMPHNA CENTER
ST. MARTIN DE PORRES CATHOLIC CHURCH

